

Protective Fencing

To be erected prior to the commencement of all works on site, and retained in place throughout construction.

Default specification: To comprise either 2.4m wooden site hoarding or a 2.5m high scaffolding framework comprising of vertical and horizontal framework, well braced to resist impacts, with uprights to be spaced at a maximum of 3.0m intervals and driven into the ground by a minimum of 600mm. On to this, standard anti-climb welded mesh panels are to be securely fixed to each other with at least two scaffold clamps and to the scaffold framework with wire.

Secondary Specification: To comprise of 2m tall welded mesh panels on rubber or concrete feet. Panels are to be joined together using a minimum of two anti-tamper couplers, installed so that they can only be removed from inside the fence. The panels should be supported on the inner side by stabilizer struts, which should be attached to a base plate and secured with ground pins.

All weather notices should be erected at regular intervals on the welded mesh panels with words such as "Construction exclusion zone - Keep out".

Tree Protection Area

KEEP OUT

Do not move this fence

TOWN & COUNTRY PLANNING ACT 1990

THREE ENCLOSURES MAY NOW BE MADE AND PROTECTED BY PLANNING CONDITIONS

ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION OF THE LOCAL PLANNING AUTHORITY

Trunk Protection

Protective trunk wrappings.

To be attached to the trunks of retained trees prior to the commencement of all works on site, and retained in place throughout construction. To comprise of a minimum of three wrappings of clean dry hessian around the trunk from ground level up to 2.2m high and held in place using sisal. Once the hessian a minimum of three wraps of overhead palling and is to be held in place by 2.50mm mild steel galvanized wire in three locations and fixed into place using fencing staples fixed into the chestnut palling.

Protective cordage:

To be erected prior to the commencement of all works on site, and retained in place throughout construction. To comprise of 2.4m wooden site hoarding constructed upon a timber frame situated around the outside of the planting pit. Where the timber frame is constructed around the tree trunk a minimum of 4 layers of clean dry hessian is to be wrapped around the trunk to protect the bark.

All weather notices should be erected with words such as "Construction exclusion zone - Keep out".

Ground boarding

New temporary ground protection should be capable of supporting any traffic entering or using the site without being distorted or causing compaction of underlying soil.

Note The ground protection might comprise one of the following:

a) for pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, or to form a suspended walkway, or on top of a compression-resistant layer (e.g. 100mm depth of woodchips), laid onto a geotextile membrane;

b) for pedestrian-operated plant up to a gross weight of 2t, proprietary inter-locked ground protection boards placed on top of a compression-resistant layer (e.g. 150mm depth of woodchips), laid onto a geotextile membrane;


c) for wheeled or tracked construction traffic exceeding 2 t gross weight, an alternative system (e.g. proprietary system or pre-cast reinforced concrete slabs) to an engineering specification designed in conjunction with arboricultural advice, to accommodate the likely loading to which it will be subjected.

For situations other than those described in a) or b), the ground boarding is to be designed by a suitably qualified person to an engineering specification in conjunction with arboricultural advice, to be able to support the expected loading to be placed upon it.

In all cases, the objective of the ground boarding is to avoid compaction of the soil beneath, so that tree root function remains unimpaired.

Construction exclusion zone

A construction exclusion zone (CEZ) is a designated area where there is to be no construction activity what-so-ever. Access to the area for construction personnel or machinery is strictly prohibited and there is no scope for materials or waste storage etc.

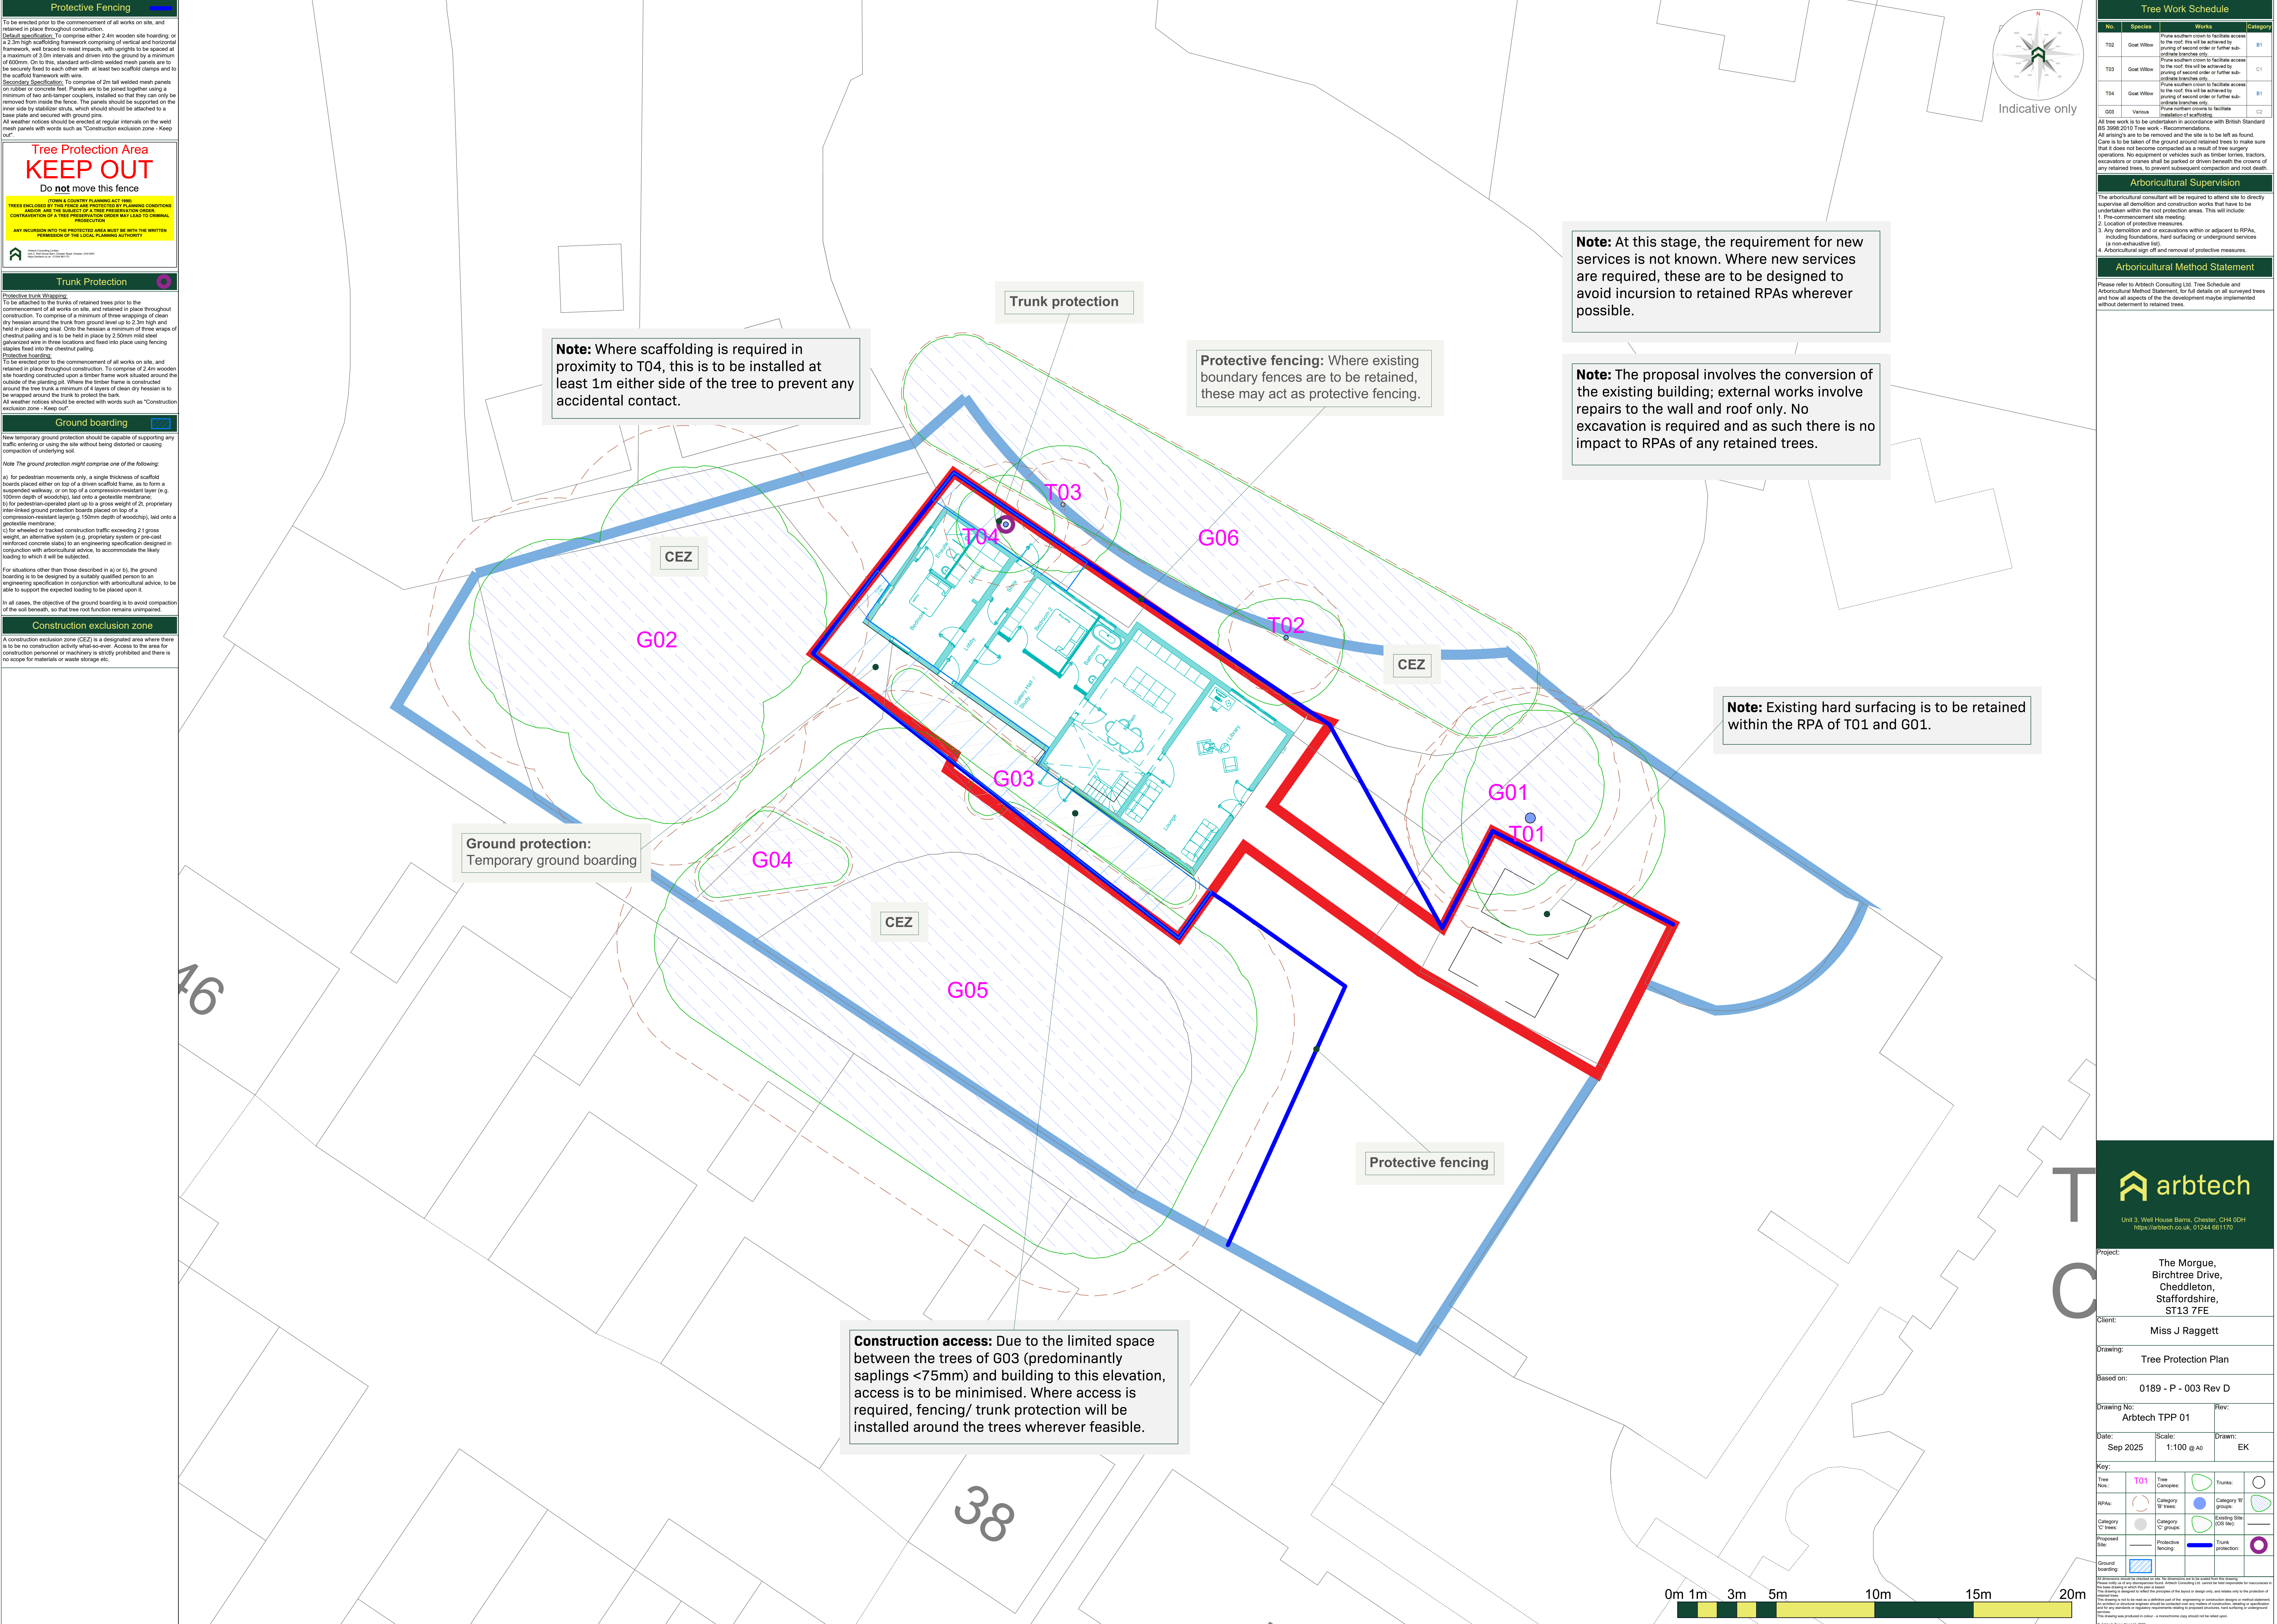

Tree Work Schedule			
No.	Species	Works	Category
T02	Goat Willow	Prune southern crown to facilitate access to the roof. This will be achieved by pruning of second order or further sub-order branches only.	B1
T03	Goat Willow	Prune southern crown to facilitate access to the roof. This will be achieved by pruning of second order or further sub-order branches only.	C1
T04	Goat Willow	Prune southern crown to facilitate access to the roof. This will be achieved by pruning of second order or further sub-order branches only.	B1
G03	Various	Prune southern crown to facilitate installation of scaffolding.	C2

All tree work is to be undertaken in accordance with British Standard BS 3988:2010 Tree work - Recommendations.

All stinging are to be removed and the site is to be left as found. Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber trailers, tractors, excavators or cranes shall be parked or driven beneath the crowns of any retained trees, to prevent subsequent compaction and root death.

Arboricultural Supervision	
The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that have to be undertaken within the root protection areas. This will include: 1. Pre-commencement site meeting. 2. Location of protective measures. 3. Any demolition and/or excavations within or adjacent to RPAs, including foundations, hard surfacing or underground services (a non-exhaustive list). 4. Arboricultural sign off and removal of protective measures.	
Arboricultural Method Statement	
Please refer to Arbtech Consulting Ltd. Tree Schedule and Arboricultural Method Statement, for full details on all surveyed trees and how all aspects of the development might be implemented without detriment to retained trees.	

arbtech

Unit 3, Well House Barns, Chester, CH4 0DH
https://arbtech.co.uk, 01244 061170

Project: The Morgue, Birchtree Drive, Cheddleton, Staffordshire, ST13 7FE

Client: Miss J Raggett

Drawing: Tree Protection Plan

Based on: 0189 - P - 003 Rev D

Drawing No: Arbtech TPP 01	Rev:	
Date: Sep 2025	Scale: 1:100 @ A0	Drawn: EK

Key:

Tree No:	T01	Tree Canopies:	Trunks:	
RPA:	Category 'B' trees:	Category 'B' groups:		
Category 'C' trees:	Category 'C' groups:	Existing Site (OS Map):		
Proposed Site:	Protective fencing:	Trunk protection:		
Ground boarding:				

Please refer to the project brief for full details of the development and the tree work to be undertaken. The drawings are to be used as a guide only and are not to be used for construction purposes. The drawings are to be used as a guide only and are not to be used for construction purposes. The drawings are to be used as a guide only and are not to be used for construction purposes.
