
Topley Pike Laboratory
Bakewell Road
Buxton
SK19 9TE

Aggregate - Estimation

Test order tTPA/00347(

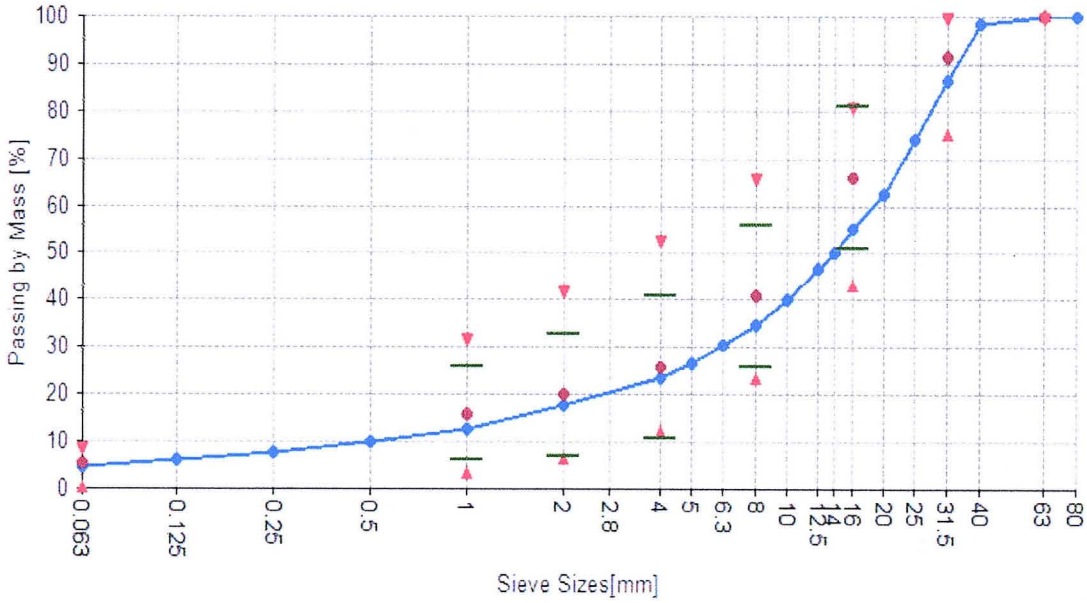

EN 1097-5: Water Content by drying in a ventilated oven			
Laboratory: Topley Pike AAL	Operator: Lucas Brough		Date of Test:27/11/20
Moist Test Portion:	5013 [g]	Dry Test Portion:	4944 [g]
mass of water:	69 [g]	Water Content:	1.4 [%]
Water content by drying in a ventilated oven	Specified max value	Declared Value	Actual value 1.40

Derbyshire, 29/11/2019

Callam Brough

Aggregates/Asphalt TS

Callam Brough

Aggregates/Asphalt TS
